


RADIATION SURVEY WORKSHEET

eXaminer Radiation Survey Information

Airport: SJU	Scanner Location: Terminal B	Case#: 356209
Personnel Performing Radiation Survey:		Date Survey Performed: 3/3/2011
Scanner Serial Number: 6193	Entrance Tunnel Serial Number: 2128 A	Exit Tunnel Serial Number: 5533 B
High Reading: 13	Average Reading: 4.55	Min. Reading: 1
High Reading: 49	Average Reading: 14.05	Min. Reading: 2
High Reading: 83	Average Reading: 16.85	Min. Reading: 1
Good	Good	Good
Radiation Meter: Type Meter: 451P	Meter Serial Number: 96	Calibration Due Date: October 27, 2011
<div style="display: flex; justify-content: space-between;"> N O T E S Complete Radiation Survey (CRS) Record Voltage and Bean Current here: </div>		
Rename this Document before starting the Survey to:		Voltage: 163769 KV
356-CRS-3MAR2011-6193		Beam Current: 9.8 mA
Maximum Safe Readings		Scanner: 350
		Tunnels: 350
		Curtains: 350
Step:	Procedure	Expected results
1.	Set Up: Obtain Inovision Ion Chamber Survey Meter and in an area away from the scanners, turn on the meter by pressing the On-Off key. Wait approx. 4 minutes for the meter to run through the initialization procedure.	The GUI will be visible and will indicate Standby. After the radiation meter initialization procedure is complete the meter will be reading less than 20 μ R/hr and the meter will be ready for use.
2.	The scanner will be in Standby. Change the conveyor switch on the scanner to Stop. Change the exit tunnel conveyor switch to Off to stop the conveyor.	Both conveyors should be stopped.
3.	On the GUI dropdown screen, select diagnostic, followed by Radiation Survey. A radiation survey window will appear. Click "Turn On" button to turn x-rays on. Turn on x-rays prompt will say "Place survey bag on belt". Place IQTK bag on Entry Conveyor Belt.	A window indicating "Radiation Survey" will appear.
4.	When "Bag in survey position" appears, go to the FCC monitor and select "2" then <Enter>, verify and record the voltage and current in the displayed on the FCC screen in the planks provided above.	The high voltage is between 144KV and 176KV . The current is between 8.8mA and 10.6mA and the scanner X-ray indicator lights are on.
5.	Survey one of the areas indicated by the boxes in Appendix A2. Record the highest reading within the area. Repeat the process until all areas are surveyed and readings are recorded.	As the survey is conducted, the radiation meter indicates the degree of radiation emission.
6.	Review all radiation data sheets for high readings.	Readings shall not exceed 350 uR/hr in any box.
7.	After radiation survey is complete, click on "Start Conveyor" button on the GUI. Click the "Turn Off" button to turn off x-rays. Next click "Done". The IQTK bag will eject from exit tunnel. EDAC will reboot.	IQTK bag is ejected and scanner reboots.
7.	Visually inspect the entrance and exit of the system for X-ray caution hazard signs.	X-ray hazard signs reading "Do not insert any part of the body when system is energized" are posted at entrance and exit of system.
9.	Fill out the eXaminer radiation sticker and adhere to to the frame of the eXaminer window #5 on the left side of the scanner.	Readings shall not exceed 350 uR/hr in any box.

RADIATION SURVEY WORKSHEET

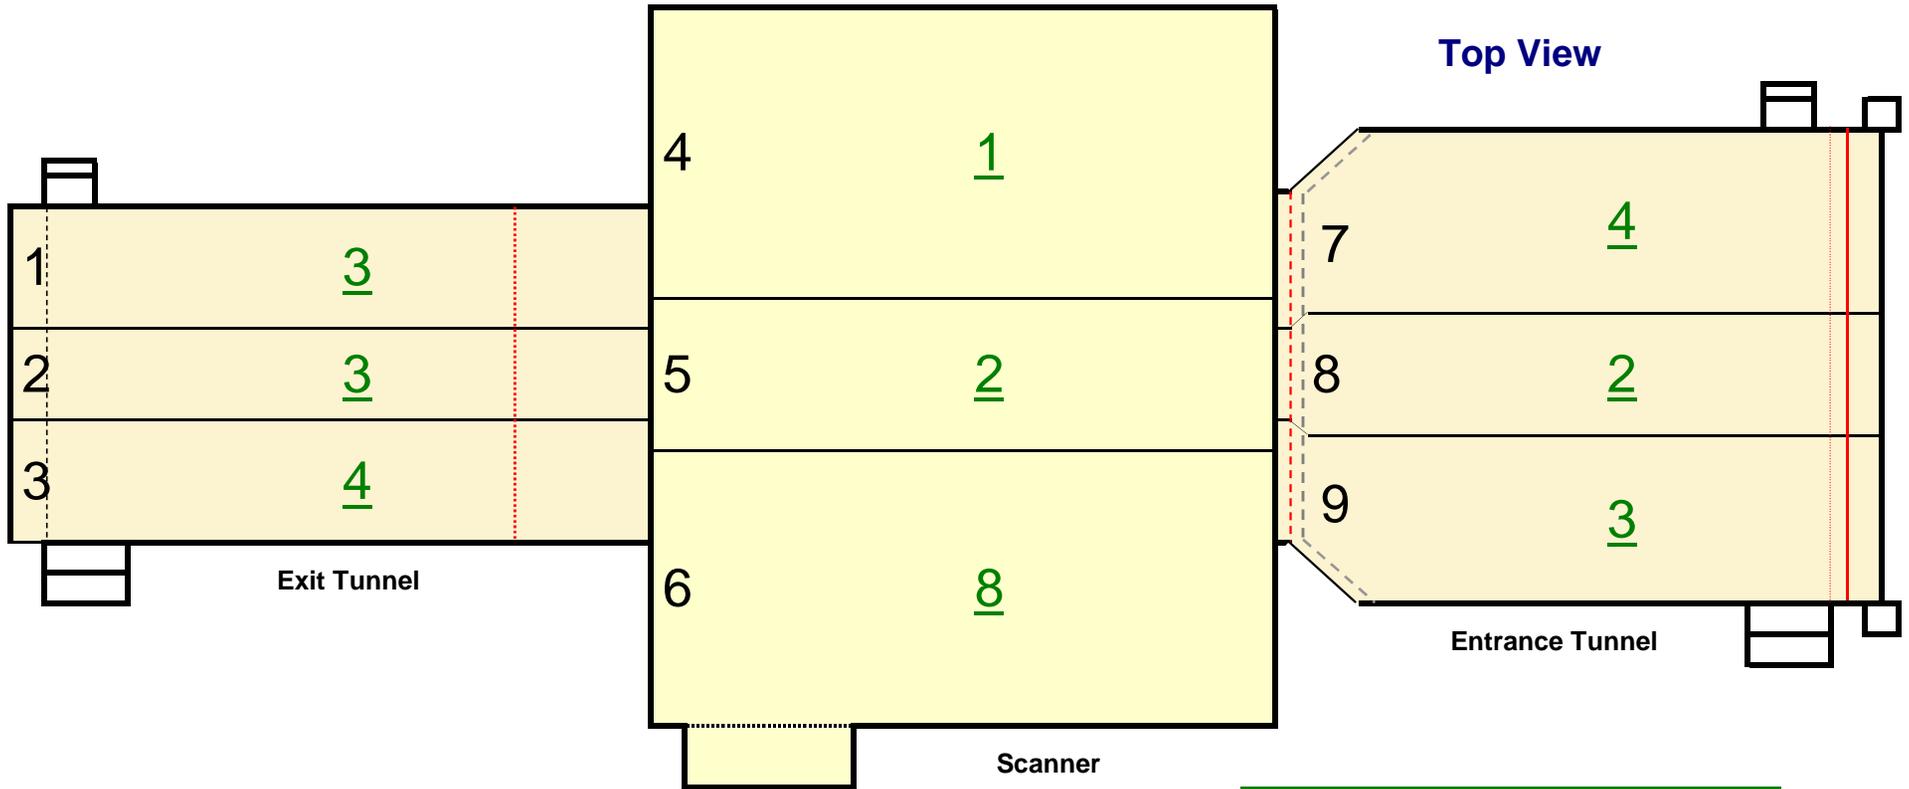


GOOD

Top View			
Scattered Radiation Measurement Points Worksheet			No PROBLEM
Record highest reading per panel		μR/Hr	
1	Exit Conveyor Top Panel	3	
2	Exit Conveyor Top Panel	3	
3	Exit Conveyor Top Panel	4	
4	Scanner Conveyor Top Panel	1	
5	Scanner Conveyor Top Panel	2	
6	Scanner Conveyor Top Panel	8	
7	Entrance Conveyor Top Panel	4	
8	Entrance Conveyor Top Panel	2	
9	Entrance Conveyor Top Panel	3	

Highest Reading	8
Average Reading	3
Lowest Reading	1

RADIATION SURVEY WORKSHEET

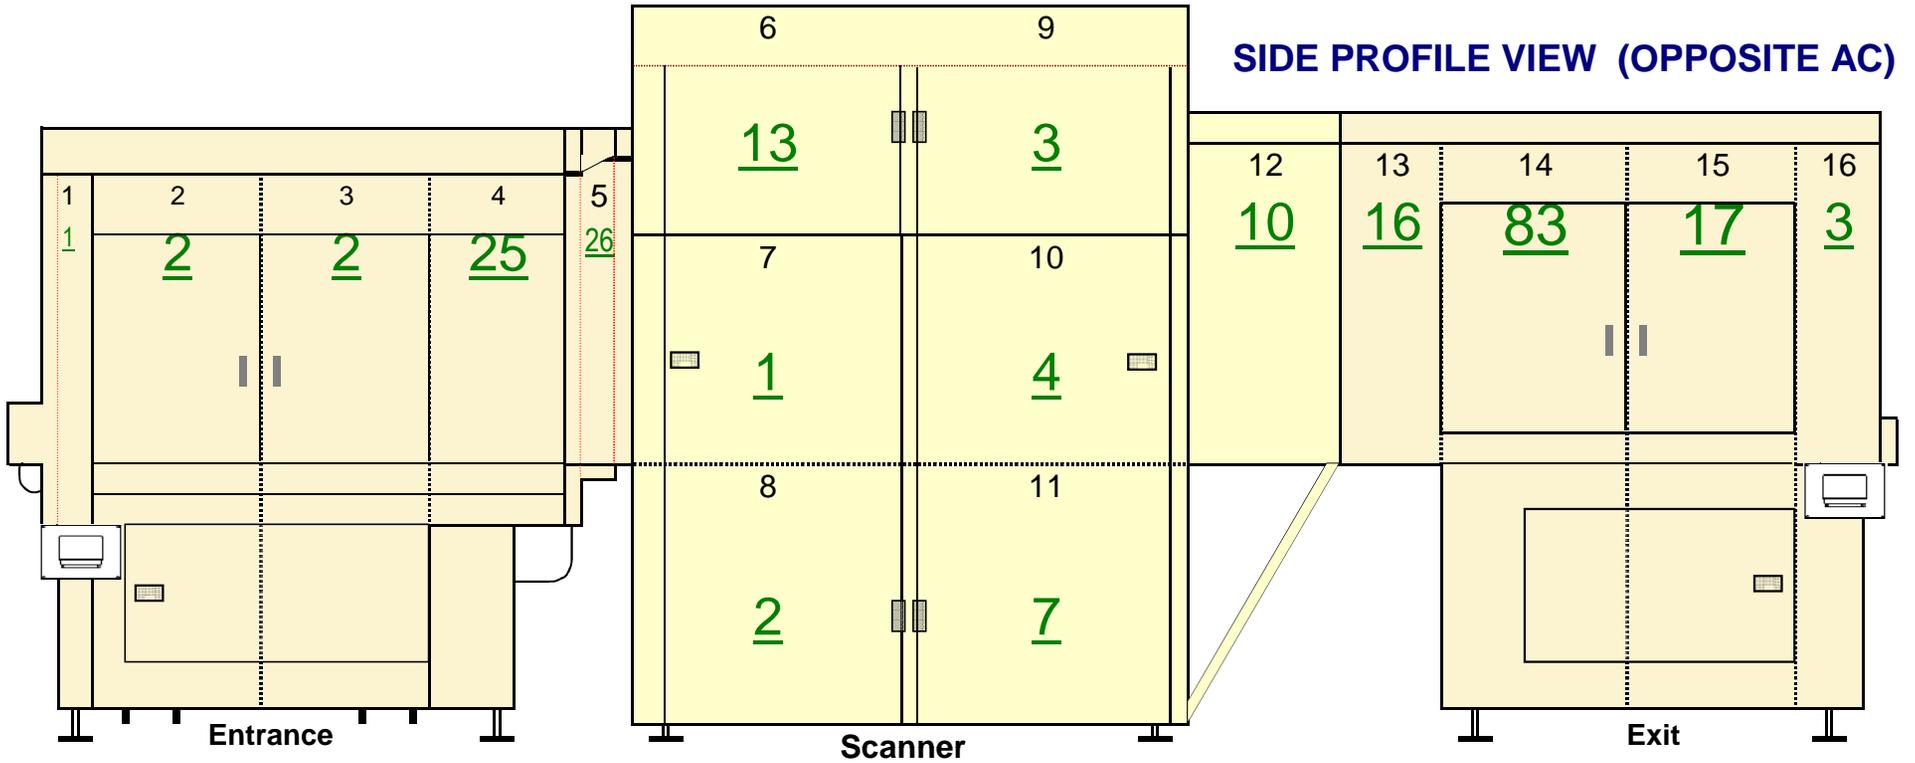


SYSTEM - SIDE PROFILE VIEW (Opposite AC Side)			
Scattered Radiation Measurement Points Worksheet			No PROBLEM
Record highest reading per panel		μR/Hr	
1	Entrance Conveyor Panel	1	
2	Entrance Conveyor Panel	2	
3	Entrance Conveyor Panel	2	
4	Entrance Conveyor Panel	25	
5	Entrance Conveyor / Scanner Panel	26	
6	Upper Scanner Panel	13	
7	Middle Scanner Panel	1	
8	Lower Scanner Panel	2	
9	Upper Scanner Panel	3	
10	Middle Scanner Panel	4	
11	Lower Scanner Panel	7	
12	Exit Conveyor / Scanner Panel	10	
13	Exit Conveyor Panel	16	
14	Exit Conveyor Panel	83	
15	Exit Conveyor Panel	17	
16	Exit Conveyor Panel	3	

GOOD

Highest Reading	83
Average Reading	13
Low Reading	1

RADIATION SURVEY WORKSHEET

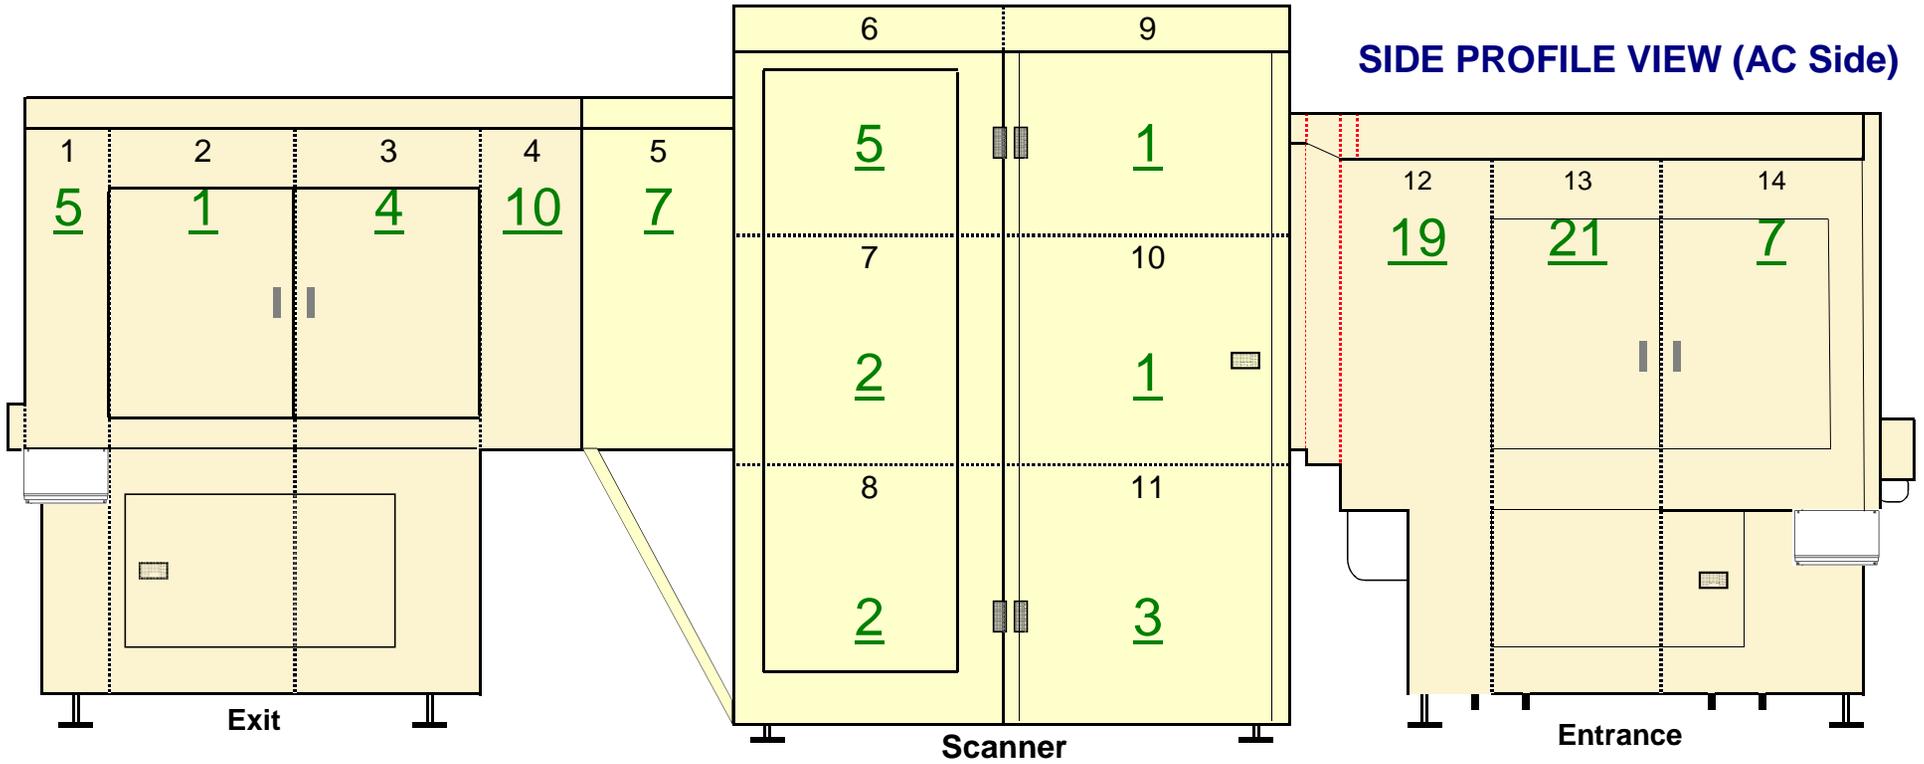



SYSTEM - SIDE PROFILE VIEW (AC Side)			
Scattered Radiation Measurement Points Worksheet			No PROBLEM
Record highest reading per panel		µR/Hr	
1	Exit Conveyor Panel	5	
2	Exit Conveyor Panel	1	
3	Exit Conveyor Panel	4	
4	Exit Conveyor Panel	10	
5	Exit Conveyor / Scanner Panel	7	
6	Upper Scanner Pane	5	
7	Middle Scanner Panel	2	
8	Lower Scanner Panel	2	
9	Upper Scanner Panel	1	
10	Middle Scanner Panel	1	
11	Lower Scanner Panel	3	
12	Entrance Conveyor / Scanner Panel	19	
13	Entrance Conveyor Panel	21	
14	Entrance Conveyor Panel	7	

GOOD

Highest Reading	21
Average Reading	6
Low Reading	1

RADIATION SURVEY WORKSHEET

SYSTEM - FACES (End Views)

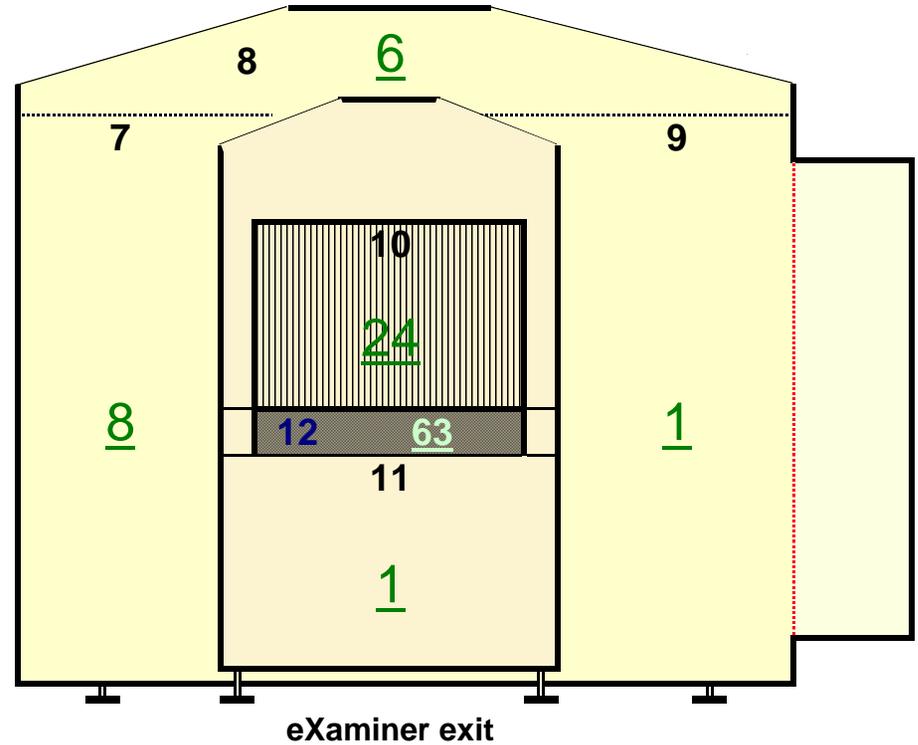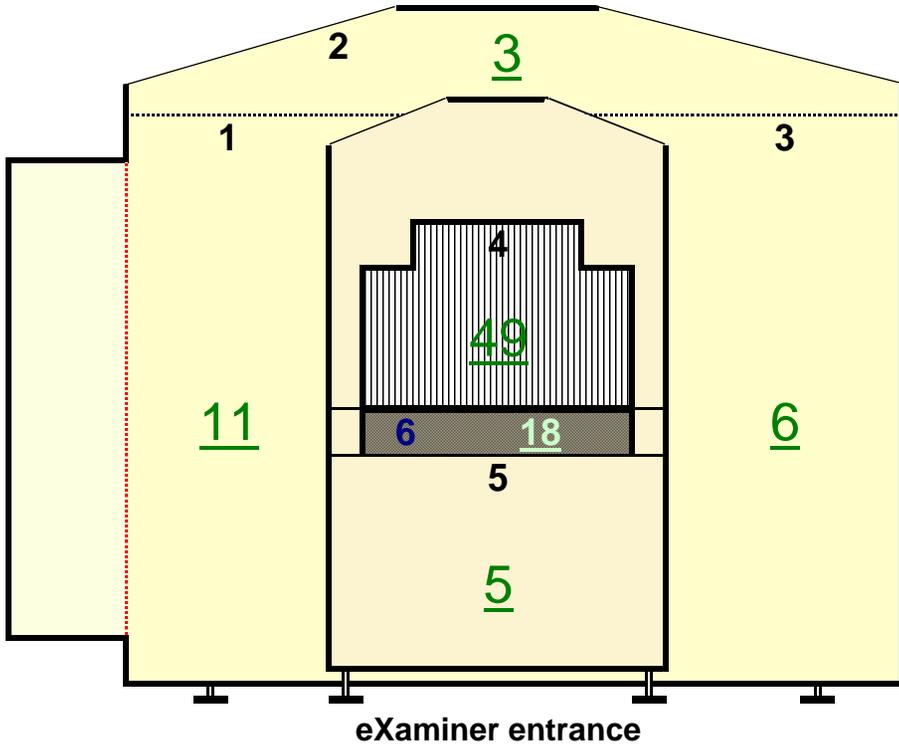

SYSTEM - FACES (End Views)			
Scattered Radiation Measurement Points Worksheet			No PROBLEM
Record highest reading per panel		$\mu\text{R}/\text{Hr}$	
1	Scanner Panel	11	
2	Scanner Top Panel	3	
3	Scanner Panel	6	
4	Belt Entrance	49	
5	Entrance Lower Panel	5	
6	Belt Lower Facia Cover Entrance	18	
7	Scanner Panel	8	
8	Scanner Top Panel	6	
9	Scanner Panel	1	
10	Belt Exit	24	
11	Exit Lower Panel	1	
12	Belt Lower Facia Cover Exit	63	

GOOD

Highest Reading	63
Average Reading	16
Low Reading	1
