Rapiscan Systems	BAGGAGE/PARCEL CABINET X-RAY SYSTEM RADIATION LEAKAGE REPORT	FIELD SERVICE ENGINEERS	Form R-0588-3 9/9/09 45. RSI W.O.# 3394182 Deferred W.O.#

1. Name of Facility: JFK INTERNATIONAL AIRPORT	2. Region: NEW YORK	3. Street Address: TERMINAL 7 C/P LN Y	
4. City: JAMAICA		5. State or Province Code: NY	6. Zip Code: 11430
7. Room No. or Other Physical Location of System: TERMINAL 7 C/P LN 4	8. Person Interviewed: [redacted]	9. Telephone Number: [redacted]	10. Fax Number: N/A
11. Manufacture Information & Certification Label Present ☒ Yes - Pass ☐ No - Fail	12. Radiation Measuring Instrument: Model: 451P-RYR Serial No. 586 Calibration Due Date: 11/24/2010 — FSE Shall Attach Copy of Calibration Certificate to This Form		
Manufacturer: Rapiscan Systems Inc.	13. System Model No. 620DVAT	14. Single Source ☐ Dual Source ☒ Other ☐, Describe:	15. System Serial No. 709/211
16. Date of Manufacture Mo. 03 Yr. 2009	18. Facility Owner Has been notified of responsibility for "Application for Registration" with their State Radiation Control Agency ☒ Yes ☐ No		19. Customer has been notified of their responsibility for posting their State "Notice to Employees" Document and Posted in Several Conspicuous Locations so Employees Can View ☒ Yes ☐ No
17. X-ray Tube Serial Number(s): P7299, P7326	20. Operator Instructions Available ☒ Yes - Pass ☐ No - Fail		21. Maintenance Schedule Available ☒ Yes - Pass ☐ No - Fail
22. Warning Label Present at Controls Stating: "Caution: X-Rays Produced When Energized" ☒ Yes - Pass ☐ No - Fail	23. Warning Labels Present at Ports Stating: "Caution: Do Not Insert Any Part of the Body When System is Energized, X-Ray Hazard" ☒ Yes - Pass ☐ No - Fail		24. Two Indicators Labeled "X-Ray On" Present at Controls (including software user interface) ☒ Yes - Pass ☐ No - Fail
25. At Least One Indicator, Marked "X-Ray On" is Visible from Each Port ☒ Yes - Pass ☐ No - Fail	26. Captured Key: The Key for the Key Actuated Control Cannot be Removed in Any Mode that Allows X-Ray Generation ☒ Yes - Pass ☐ No - Fail		
27. All Doors and Access Panels To the X-Ray Beam Prevent Generation of X-Radiation ☒ Yes - Pass ☐ No - Fail	28. Some Part of the Body Can Be Inserted Through a Port Into The Primary Beam ☐ Yes ☒ No		
29. Use of X-Ray Control Necessary to Resume Operation Following Interruption ☒ Yes ☐ No	30. Means Provided to Ensure Operator Presence at the Control Area X-ray located in a public access area ☒ Yes - Pass ☐ No - Fail Or X-ray located in a non-public access area ☐ Not Required		
Rapiscan Systems Test Procedure Used: Rapiscan Systems WI-0023-4	31. Scatter Block Description: ☐ Two (2) Reams Copy Paper ☒ Other, Describe: METER CASE	32. Means Provided to Operator for Terminating Exposures of Greater than One-Half Second and Preventing X-rays (E-Stop Test) ☒ Yes - Pass ☐ No - Fail	
33. X-Ray Generator Settings: 160 kVp 1.000 mA	**Note: All Survey Measurements Shall be Obtained at 5 cm from All External Surfaces and at 5 cm from the Plane of All Access Port Openings or Shroud Extension Openings. Scatter Block shall be Stacked and Positioned Centerline of Primary Beam.**		
34.1. Background Radiation: 1 uR/hr	--	**Maximum External Surface Dose Rate Not to Exceed 500 uR/hr at 5 cm from all external surfaces.**	

34.3 Record All Readings in uR/hr Unless Otherwise Noted

Please see model specific diagram (attached)

36. Overall Condition of Lead Drapes: ☒ SAT - Pass ☐ UNSAT- Fail Description	37. Overall Condition of Machine: ☒ SAT – Pass ☐ UNSAT – Fail	38. Comments, Corrective Active Actions and/or Recommendations: N/A

39. Surveyor Name (Print: L, F, MI): [redacted]	40. Surveyor Signature: [redacted]	41. Date of Survey: 10/4/10	42. Time of Survey:
The Surveyor has inspected, tested and certified this x-ray machine is in compliance with U.S. FDA 21 CFR 1020.40 and equivalent international radiation emission leakage standards.	43. [redacted]) have received a copy of this Radiation Survey Report and understand the responsibility to retain this report for State inspection. Signature: [redacted] Date 10/4/10		

This report is to certify this x-ray unit has been surveyed for radiation leakage emissions and found to be within the regulatory radiation emission limit. The safety features, controls and indicators incorporated in the x-ray unit have been satisfactorily tested and/or inspected. The owner of this x-ray unit is responsible for State Radiation Control Agency compliance (not applicable for facilities exclusively operated by the Federal Government) and for the safe use and routine inspection, general maintenance and cleanliness of this x-ray unit. Only trained and qualified individuals should operate this equipment.

OC 58938
(m) 3394182

Rapiscan systems	MODEL 620DV OR 500 SERIES EQUIVALENT RADIATION LEAKAGE SURVEY FORM	MODEL 620DV FSE SURVEY FORM	FORM FSE-R-0047-620DV-1

FIELD SERVICE ENGINEERS RADIATION EMISSION SURVEY

United States and Canada External Surface Radiation Leakage Limit is 5.0 uSv/hr at 5 cm (500 uR/hr)

Global External Surface Radiation Leakage Limit is 1.0 uSv/hr at 5 cm (100 uR/hr at 5 cm)

Date: 10/4/10	Location Manufactured: (Check One) ___ Malaysia ___ UK ✓ US	Instrument Model No: 451P-RYR
Time:	Date of Mfg: 03/2009	Instrument Serial No: 7091211
Background: ___ uSv/hr (1 uR/hr)	Serial No: 7091211	Instrument Calibration Due: 11/24/2010
All Measurements Recorded In: ___ uSv/hr ✓ uR/hr (Check One)	Settings: 160 kvP 1.000 mA Settings: 160 kvP 1.000 mA	Description of Scatter Body: (Check One) ___ Paper (2 Reams, 500 sheets each) ___ Wood Block (4" x 4" x 12" L) ✓ Other METER CASE

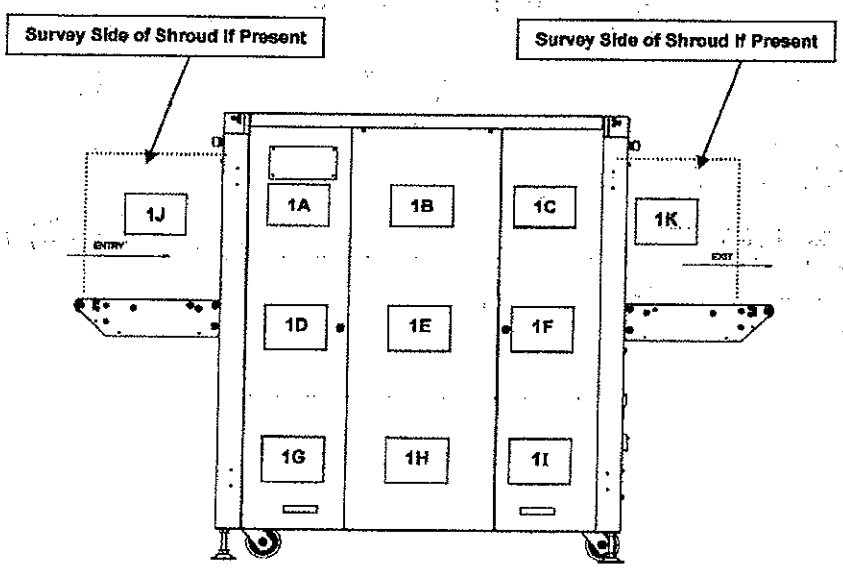

Operators Side

Location	Results NO Scatter Body	Results WITH Scatter Body
1A	6	8
1B	5	10
1C	3	12
1D	7	14
1E	8	22
1F	6	28
1G	4	8
1H	2	10
1I	3	9
1J	13	24
1K	16	18

[redacted]

FIELD SERVICE ENGINEERS RADIATION EMISSION SURVEY

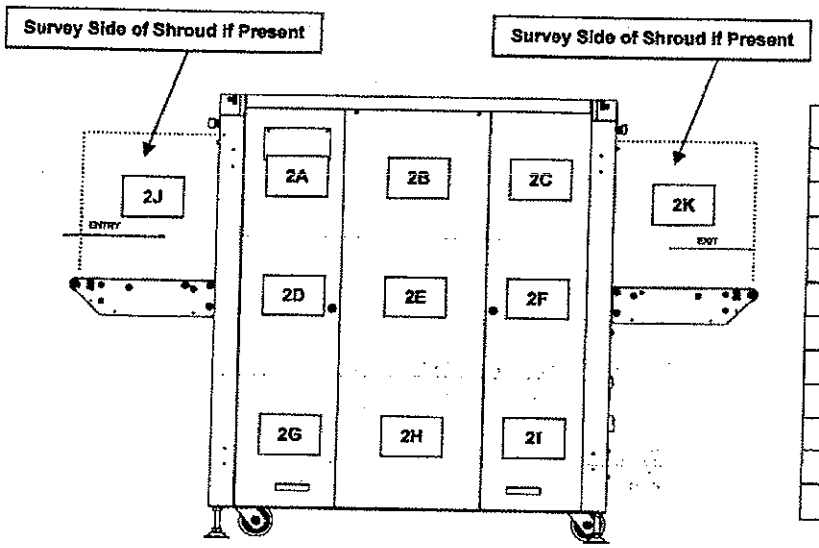

Non-Operators Side

Location	Results NO Scatter Body	Results WITH Scatter Body
2A	14	27
2B	16	26
2C	13	23
2D	19	19
2E	13	20
2F	15	18
2G	14	18
2H	13	16
2I	10	13
2J	11	16
2K	18	12

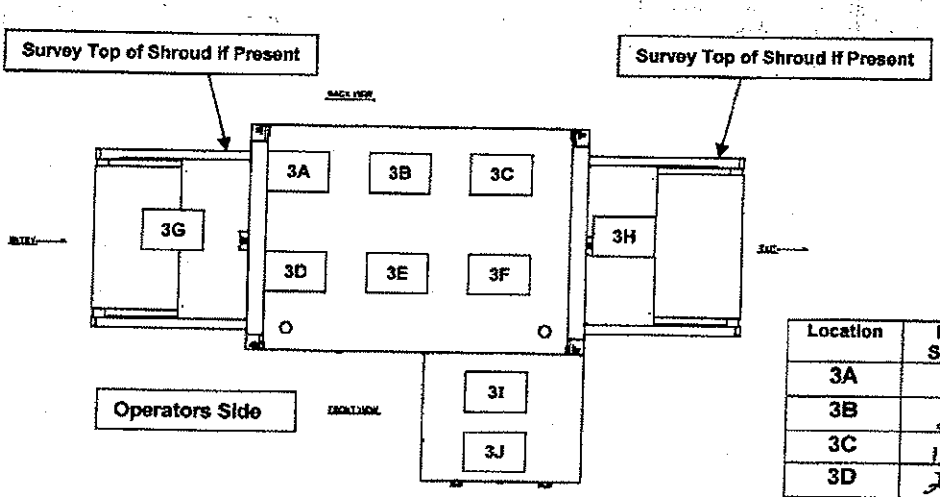

Top View

Location	Results NO Scatter Body	Results WITH Scatter Body
3A	18	21
3B	23	25
3C	17	14
3D	20	14
3E	16	18
3F	13	17
3G	20	29
3H	38	37
3I	39	36
3J	41	29

FIELD SERVICE ENGINEERS RADIATION EMISSION SURVEY

EXIT TUNNEL

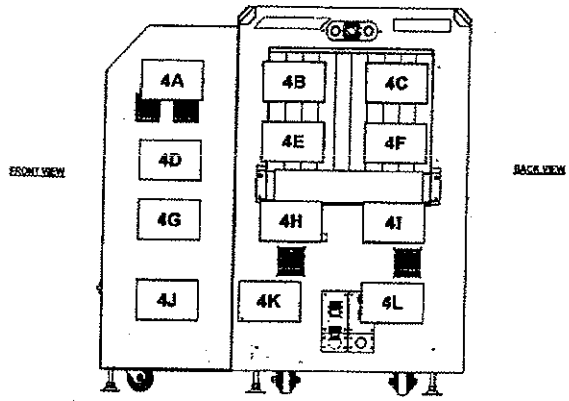

Location	Results NO Scatter Body	Results WITH Scatter Body
4A	19	27
4B	33	63
4C	37	62
4D	23	28
4E	31	64
4F	35	93
4G	28	26
4H	19	15
4I	17	19
4J	22	15
4K	13	18
4L	8	10

ENTRANCE TUNNEL

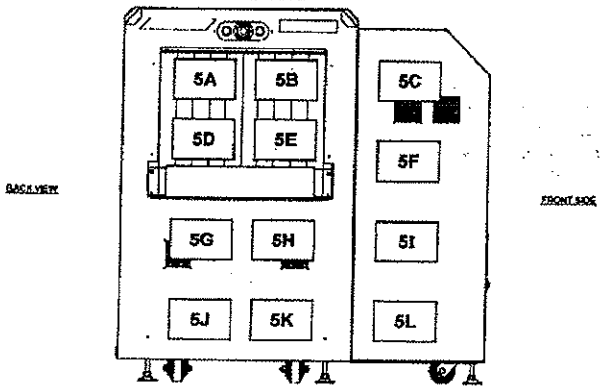

Location	Results NO Scatter Body	Results WITH Scatter Body
5A	30	78
5B	33	49
5C	18	9
5D	41	60
5E	35	68
5F	24	22
5G	21	23
5H	17	21
5I	6	14
5J	11	29
5K	18	18
5L	12	17

Instructions:

- If shrouds are NOT installed, radiation measurements shall be taken 5 cm from the lead drapes.
- If shrouds are installed, radiation measurements shall be taken at the imaginary plane of the shroud opening.
- Lead Drapes should touch the conveyor. If they do not, check to verify x-ray radiation is not traveling down the conveyor where the gap exists between the lead drapes and the conveyor surface.
- Survey below the conveyor up against the cabinet near any gaps, mating surfaces, and photo sensor cut-outs.

SURVEY PERFORMED BY [redacted] DATE: 10/4/10

[redacted]
